

St Andrews Primary School

PROGRESS REPORT 3 | 10th Aug 2026

Works completed on site over the last fortnight


- Drainage throughout boys & girls WC , male staff WC, Female staff WC, staff unisex DDA, first aid are ready for inspection
- Walls framed throughout boys & girls WC including openings
- North elevation external walls framed
- Perimeter reception, first aid, BM office & delivery room framed
- Sensory room entry framed
- Electrical cabling removed from existing steel beams

Anticipated works next Fortnight

- Drainage inspection potentially Monday afternoon
- Start gas relocation for drainage to future kitchenette
- Steel approval & installation
- All internal groundworks & packing sand to start plumbing rough in
- Continue frame where possible
- Roofing Delivery — Crane 14.08.2026 (Student free day)
- Concrete Infill trenches
- Brickwork footings
- Gas relocation

Information and items required for upcoming works




- See RFI's & meeting agenda items discussed

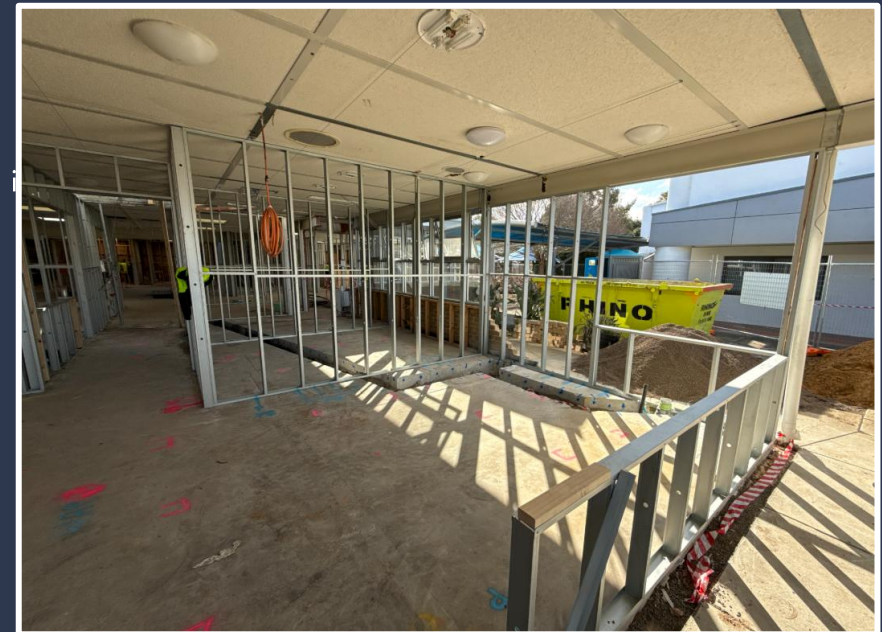

SEE OUR PROJECTS
@jointly_built






building **Victoria**

St Andrews Primary School

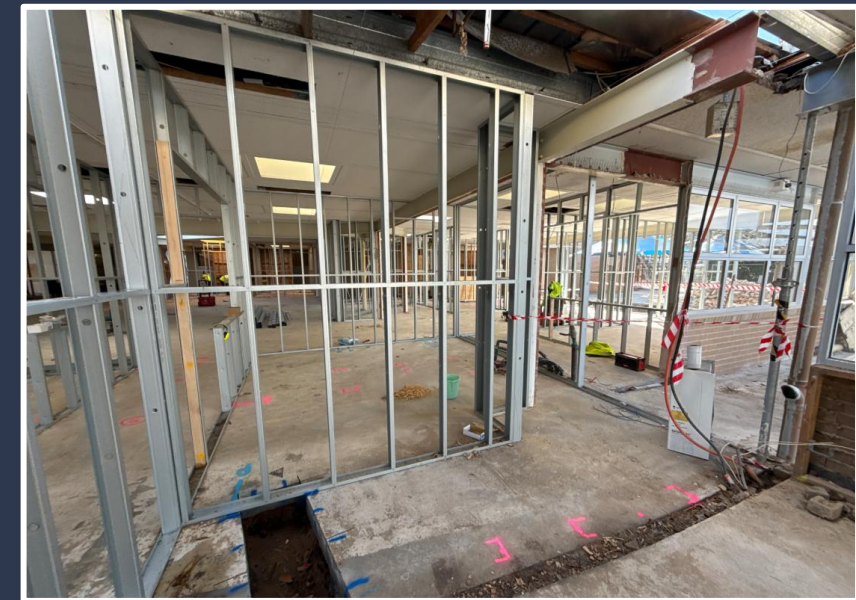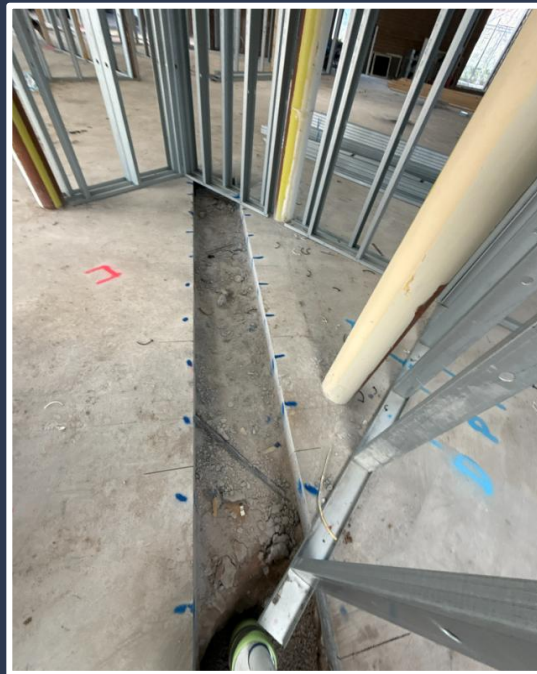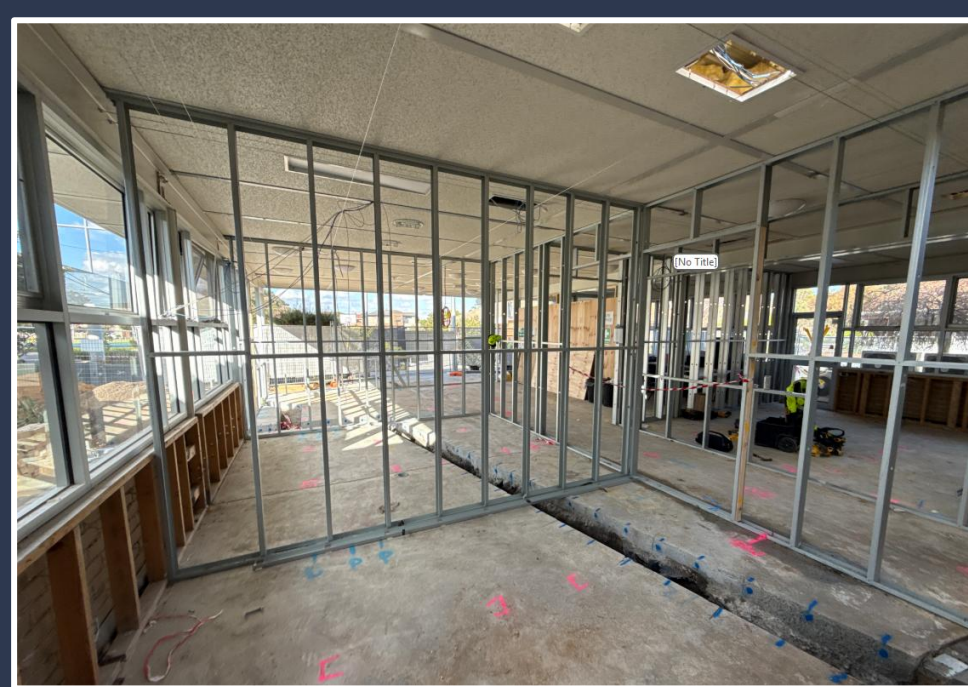

St Andrews Primary School

PROGRESS REPORT 3 10th Aug 2026

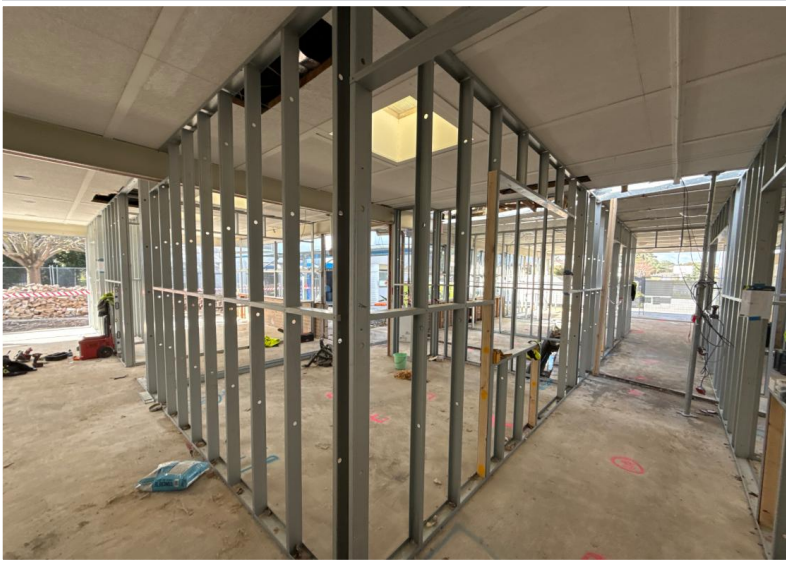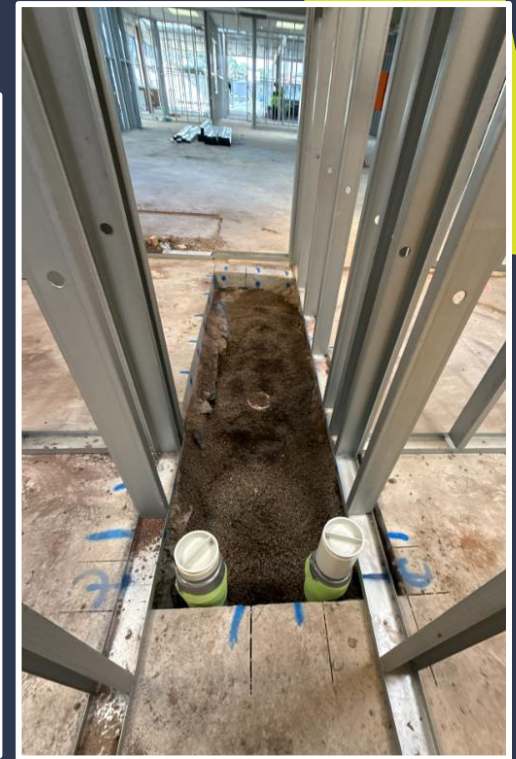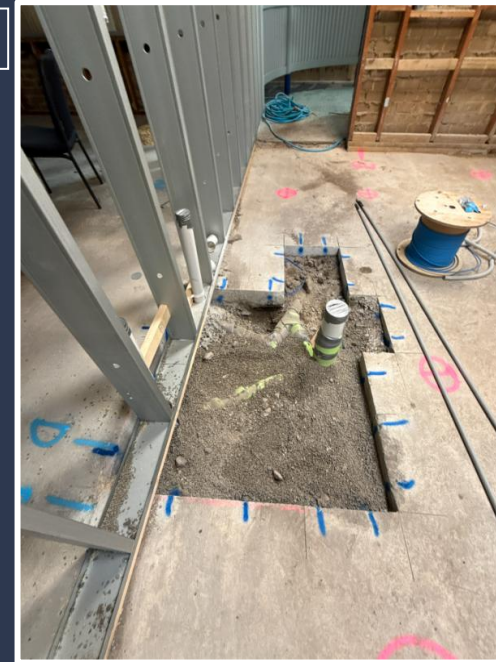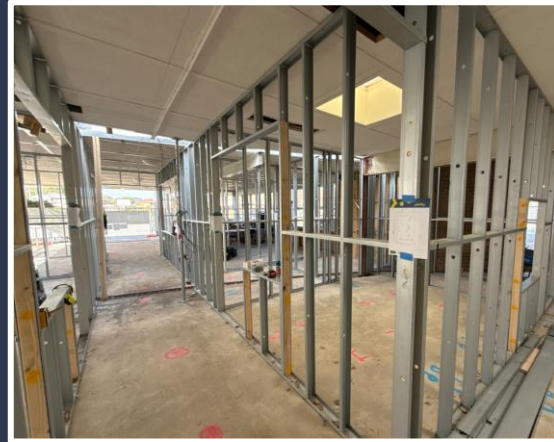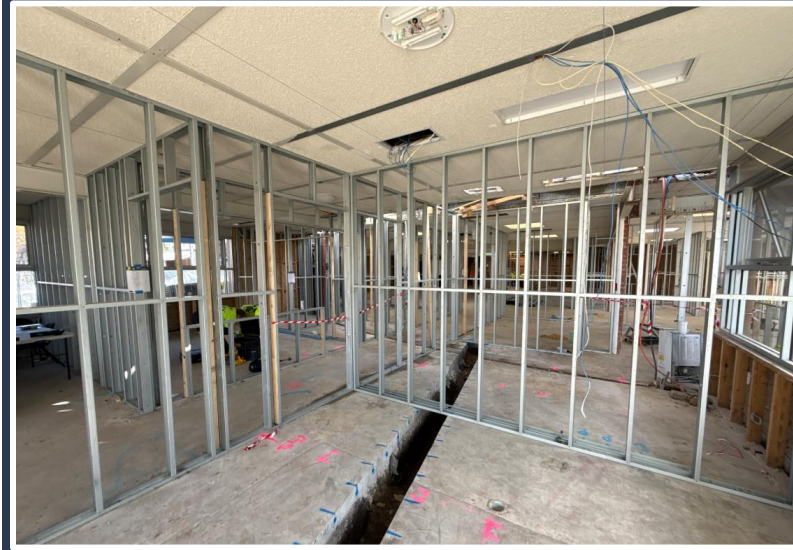

SEE OUR PROJECTS
@jointly_built

building Victoria
