

# St Andrews Primary School

PROGRESS REPORT 5 | 29th Sept 2026

## Works completed on site over the last fortnight

- Electrical rough-in is 95% complete.
- Plumbing rough-in is 95% complete.
- All carpentry lock-up works have been completed.
- Mechanical rough-in works are continuing.
- Brickwork is 90% complete.
- General site clean-up has been carried out.
- Concrete cutting in the courtyard area of the new entranceway has been completed.
- Internal existing window painting is underway.
- Internal beam painting is underway.
- Window installation, including glass, is underway.

## Anticipated works next Fortnight

- Plastering works will commence (walls only)
- Roof works will commence
- Window installation will continue
- Painting of beams and windows will continue
- Concrete will be removed from the courtyard


## Information and items required for upcoming works

- See RFI's & meeting agenda items discussed



# St Andrews Primary School



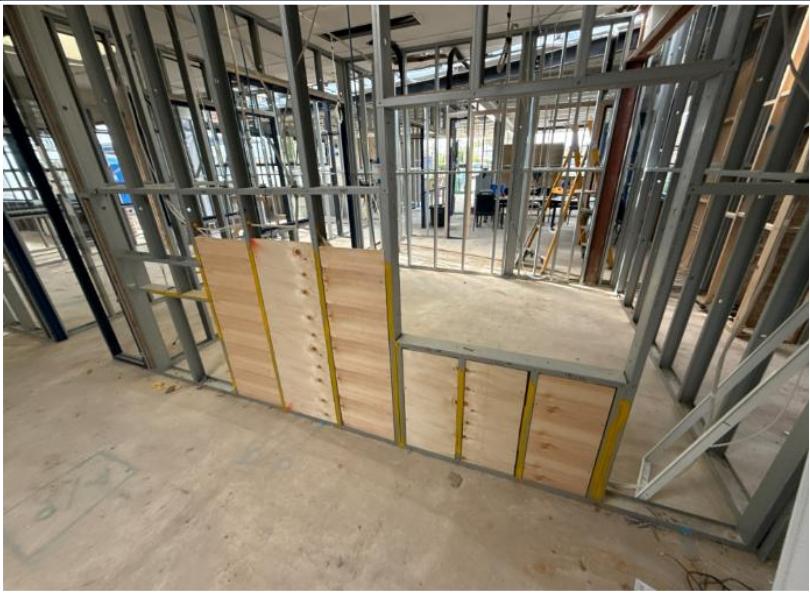

SEE OUR PROJECTS  
@jointly\_built

